



2018-19 REHABILITATION SEAL COAT PROJECT (NORTHCREST ESTATES AREAS, LAGO VISTA AND W. CONSTITUTION STREET)

Project Description: The scope of the project includes reconstruction of W. Constitution Street with lime-stabilized subgrade, geo-grid 8" of limestone base and a two-course seal coat. Northcrest Estates and Lago Vista consists of a single seal coat with a Grade 5 trap rock and an application of Onyx over the seal coat. The Onyx application is a frictional mastic surface treatment, which provides added durability, reduces aggregate shelling and minimizes oxidation to the seal coat. The application of Onyx is replacing the previous process used of applying a double seal coat.

Start Date: 4/15/2019


Estimated Completion: 4/14/2020

Contractor: Brannan Paving Co., LTD

Engineering Firm: COV

Construction Cost: \$ 1,735,288.00

Percent Complete: 86% Complete

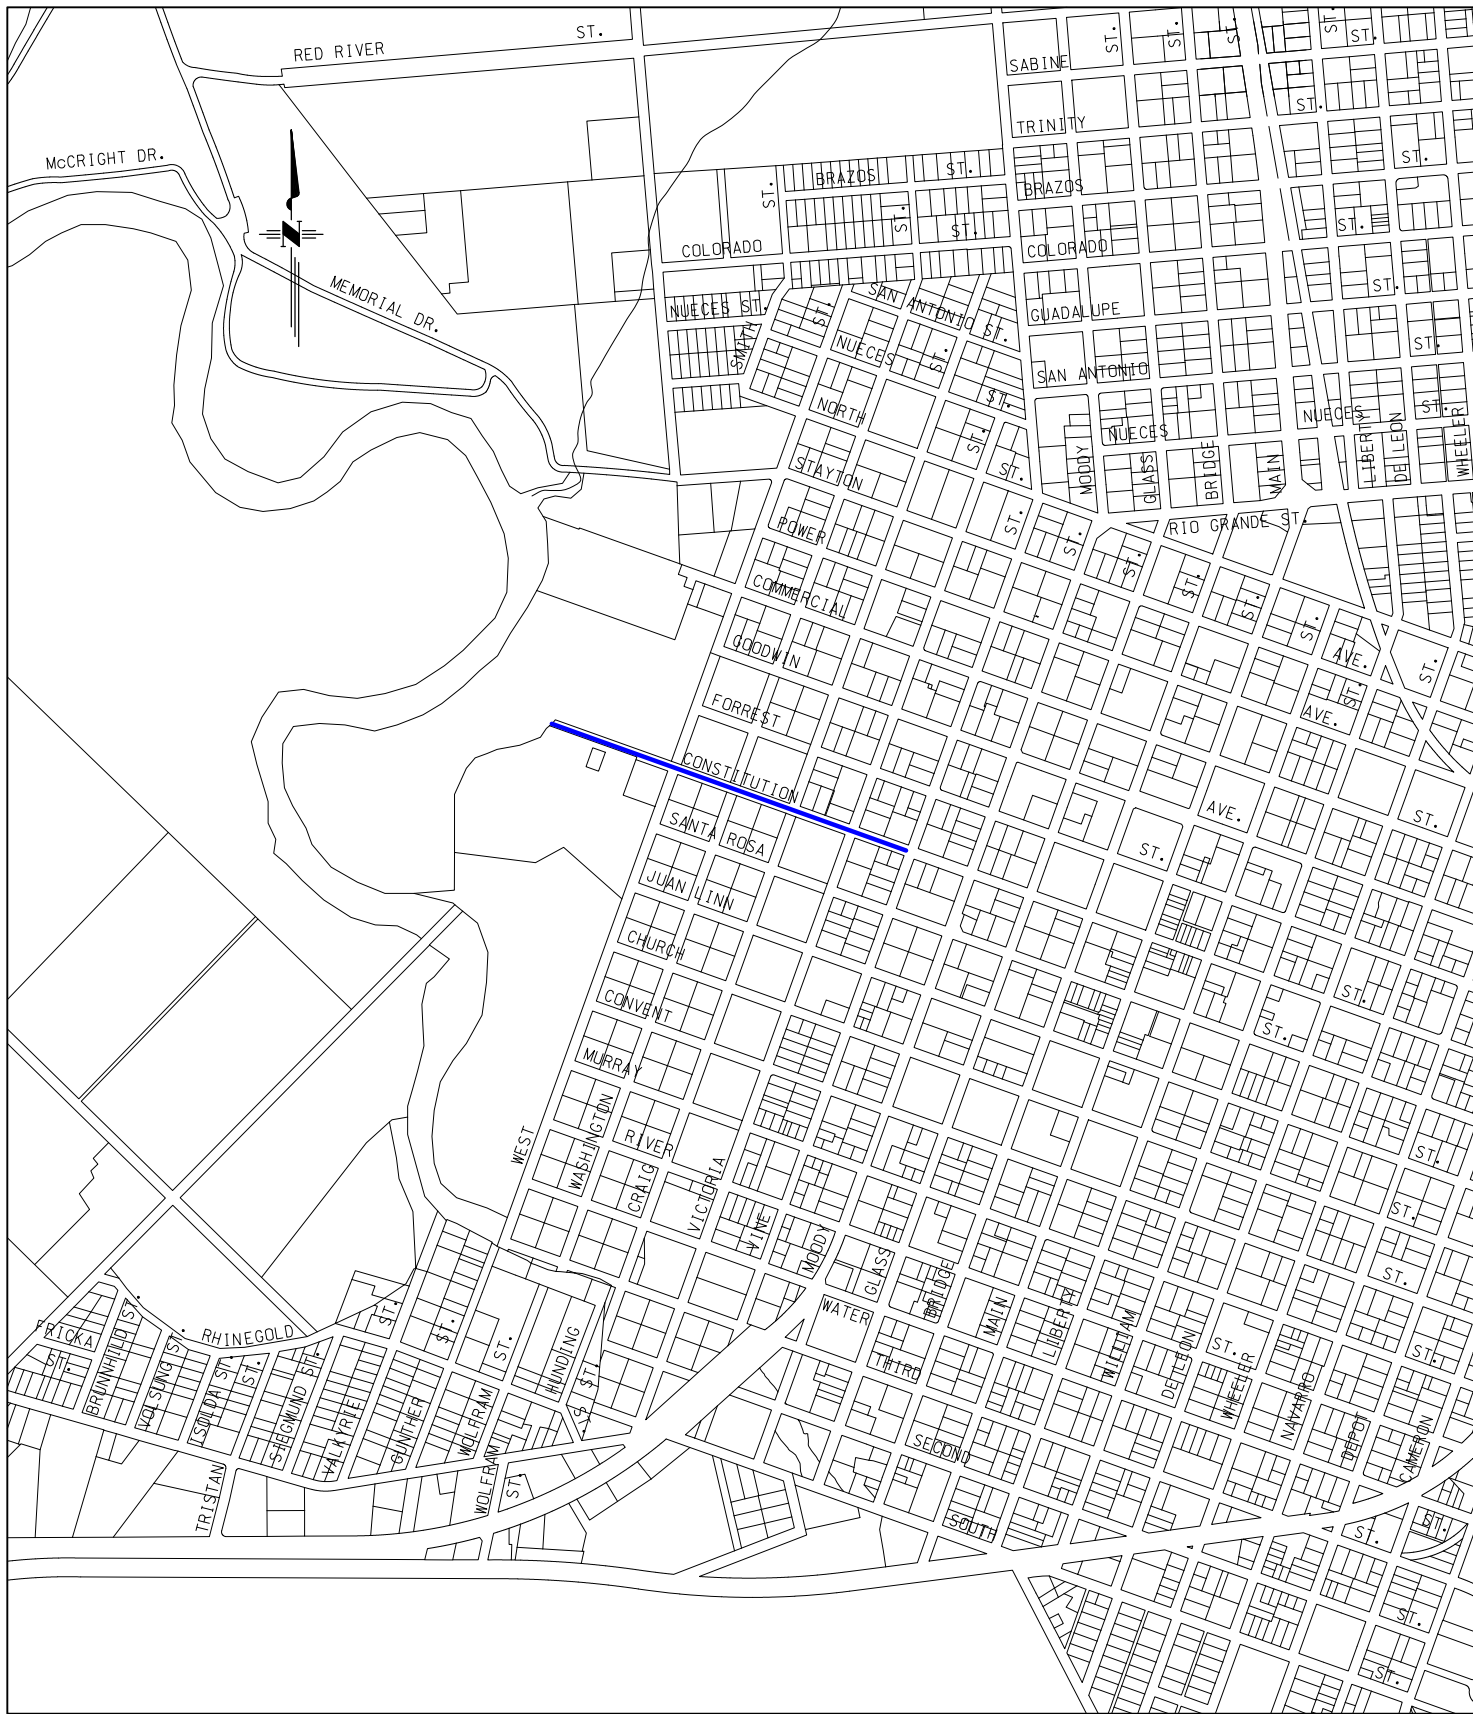

700 MAIN CENTER
SUITE 201
VICTORIA, TX 77901

CITY OF VICTORIA
ENGINEERING DIVISION
P.O. BOX 1758
VICTORIA, TX 77902-1758

**2018-19 SEAL COAT AND REHAB PROJECT
(NORTHCREST ESTATES AREAS, LAGO VISTA
AND W. CONSTITUTION STREET)**

DRAWN BY: J. GONZALES

**DATE: 1/25/19
REV'D:
SHEET: 2 OF 2**

PROJECT
